Future Flexible Acquisition & Sustainment Tool

WR-ALC/PK

FAST

5th

F²AST Information Exchange

08 May 07

Debbie H. Jackson
FAST Program Director
WR-ALC/PKF

Overview

WR-ALC/PK

- Welcome
- Current Status
  - Data Analysis
  - Web Site
- Important Contract Policy
- Future Status
  - Schedule
- Summary

Welcome

WR-ALC/PK

- 5th F2AST Information Exchange
- Purpose
  - Open lines of communications
  - Contractor Feedback
  - Provide you with updated information as we know it
- Please check your name on sign in sheet or add it if not already there

Overview

WR-ALC/PK

- Welcome
- Current Status
  - Data Analysis
  - Web Site
- Important Contract Policy
- Future Status
  - Schedule
- Summary

Current Status (Data Analysis/Data Gathering)

- Data Analysis / Gathering /Mining Continues
  - Scope
  - Ceiling
  - Requirements
  - Number of Awards
  - Past Performance

Original Anticipated Scope

- Development
- Modifications
- Spares
- Repairs
- Services
  - A&AS
  - Other

5 Categories Of Work

Scope – Development

WR-ALC/PK

- Not develop the next generation aircraft
  - Modify current weapon systems and/or their subsystems

Scope – Modifications

WR-ALC/PK

- Modify current weapon systems and/or their subsystems
  - Enhancements
  - Reliability
  - Serviceability
  - Maintainability
  - Performance

Scope – Spares

WR-ALC/PK

- Initial Spares
- Contingency Spares
  - Short term customer requirement
- Limited Spares
  - Low fielded population
  - Low demand rate
- Critical Spares

Scope – Repair

WR-ALC/PK

- Contingency Repair
  - Short term customer requirement
- Limited Repair
- Critical Repair

Scope – Services A&AS

WR-ALC/PK

- Any work that can be accomplished by 2 or more Small Businesses be “removed from the scope of F²AST”

<u>Based on Market Research and Historical Data</u>

- 2 or more Small Businesses have and can accomplish this work
  - Work not integral to a program
    - Logistics Services, Engineering Services, Other Services, etc
    - **STRAIGHT MANPOWER – Organic Augmentation**
- Removed PE “A&AS” types of work from scope

From This Point Forward

Scope – Services Other

WR-ALC/PK

Predecisional

Based on Market Research and Historical Data

- 2 or more Small Businesses have and can accomplish this work
  - Aircraft Inspections, DMS, Logistics, Technical Documentation, Software, etc
- Investigating Small Business Set Aside

(Data Analysis/Data Gathering)

Anticipated Scope

WR-ALC/PK

Predecisional

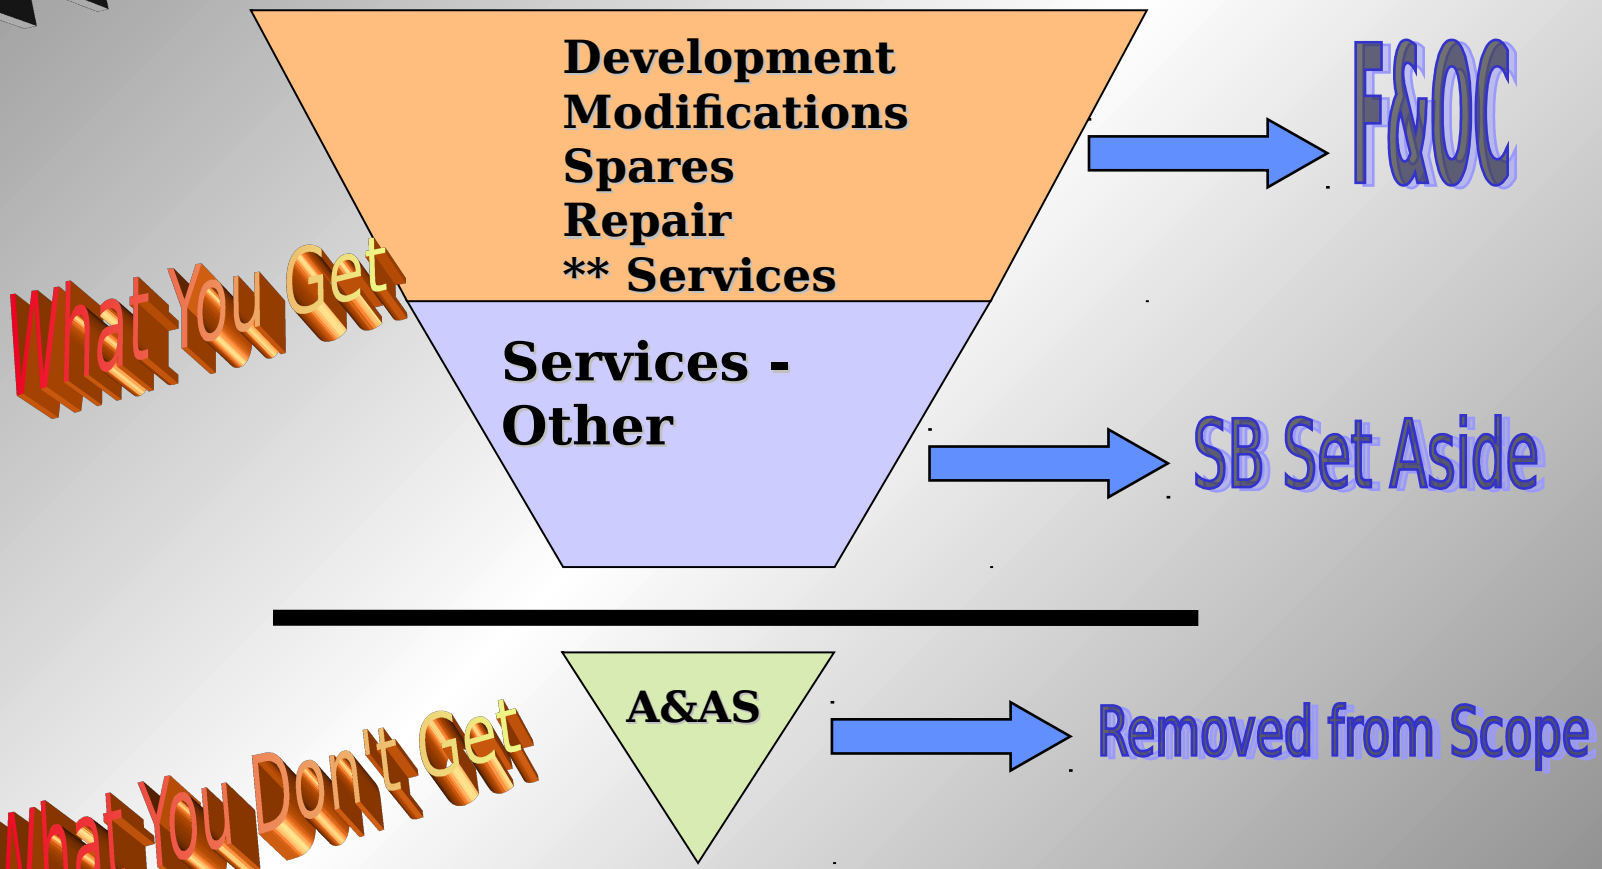

(Data Analysis/Data Gathering)

Funding Ceiling

WR-ALC/PK

- FO&C
  - $6.2B
    - F²AST
      - $4.0B
    - IWSSP
      - $2.2B
    - Based on 8 year ordering period and 10 year PoP
- SB Set Aside – Other Services
  - $250M
    - Based on 5 year PoP

(Data Analysis/Data Gathering)

Requirements – F&OC

WR-ALC/PK

- Capabilities Matrix
  - Technically Acceptable
    - Certifications
    - Facilities
    - Engineering
    - Processes
    - Equipment
    - Training
    - Manpower
  - Prime + 4 significant subcontractors must have capabilities in each category of work
  - Go/No Go Decision

Predecisional

(Data Analysis/Data Gathering)

Past Performance – F&OC

WR-ALC/PK

- Prime + 4 significant subcontractors
  - Must have capabilities in each of the categories of work
    - 21 MAXIMUM
- Prime's Management of Subcontractors
- Questionnaires ?

Predecisional

(Data Analysis/Data Gathering)

Requirements – Set Aside

WR-ALC/PK

- Capabilities Matrix
  - Technically Acceptable
    - Certifications, Equipment, Facilities, Engineering, Processes, Training, Manpower
  - Prime + 4 Significant subcontractors
    - **Prime or 1 of the 4 significant subs must be able to do at least 50% of the work**
  - Go/No Go Decision

Predecisional

(Data Analysis/Data Gathering)

Past Performance - Set Aside

WR-ALC PK

- Standard Past Performance Process and Relevancy Determination
  - Questionnaires

(Data Analysis/Data Gathering)

Awards

WR-ALC/PK

- FO&C
  - Anticipate up to X
- SB Set Aside
  - Anticipate up to X

(Data Analysis/Data Gathering)

Strategy

WR-ALC/PK

- Technically Acceptable
  - Capabilities Matrix
- Performance
- Price

PKEC Web Site Update

WR-ALC/PK

- Based on new policy, individual organization's public web sites are being shut down
  - Web site still running (so far) – print what you need

Overview

WR-ALC/PK

- Welcome
- Current Status
  - Data Analysis
  - Web Site
- Important Contract Policy
- Future Status
  - Schedule
- Summary

Contract Policy

WR-ALC/PK

- **TOPIC:** Excessive Pass-Through Charges
- **REFERENCE:** Federal Register, 26 Apr 07
- **SUMMARY:** DoD issued an interim rule that amends DFARS Parts 215, 231 and 252. This rule implements Section 852 of the FY 2007 NDAA. It requires offerors and contractors to identify the percentage of work that will be subcontracted and, when subcontract costs will exceed 70 percent of the total cost of work, to provide information on indirect costs and profit and value added with regard to the subcontract work. Contracting Officers should familiarize themselves with the new regulations regarding excessive pass-through charges.
- **POC:** SAF/AQCP

Contract Policy

WR-ALC/PK

- **TOPIC:** Limitation on Subcontracting
- **REFERENCE:** FAR 52.219.14 (Policy Memo 2006-PK-04 (19 Oct 2006)
- **SUMMARY:** IAW FAR 52.219-14(b)(1), Limitations on Subcontracting (1996), for services (except construction), a concern may not be awarded a contract as a small business concern unless at least 50% of the cost of contract performance incurred for personnel is expended for employees of the concern. The Small Business Administration (SBA) regulations allow the cooperative efforts of joint ventures (formal or informal) in meeting the subcontracting limitations requirement. A recent ruling by the SBA stated that an informal joint venture is not presumed for each prime and subcontractor relationship. Further, any informal joint venture relationship must be evidenced by an agreement between the business concern explaining that the relationship is a joint venture and meets the Code of Federal Regulation's (CFR) definition of joint venture.
- **POC:** AFMC/PKPA

Overview

WR-ALC/PK

- Welcome
- Q&A Feedback
- Current Status
  - Data Analysis
  - Web Site
- Contract Policy
- Future Status
  - Schedule
- Summary

Future Status

WR-ALC/PK

- Begin acquisition strategy approvals thru chain of command
  - Draft Executive Summary in work
  - ASP tentatively scheduled for 16 Aug

Internal Schedule

WR-ALC/PK

EVENT	DATE
• REQUIREMENTS DEFINITION	31 OCT 06
• MARKET RESEARCH	20 DEC 06
• ACQUISITION PLANNING	JAN-JUL 07
• ASP	AUG 07
• RFP	SEP 07

Aggressive

Draft Schedule

Summary

WR-ALC/PK

- Meeting Schedule
  - Next 2 mtgs moved to 3rd Tuesday based on availability of Vista Scope
    - 19 Jun, 2pm
    - 17 Jul, 2pm, if needed
  - 14 Aug, 2pm, if needed
